Prabu Shankar P
ROLL NO 241501142

EXPERIMENT 11

Development to production deployment

Aim

Prepare and verify a controlled release of the application through the environments your account supports.

Procedure

1. Confirm whether Development, Stage and Production environments exist. If not, document a design-only release using separate test and live apps.
2. Prepare release 1.0: change list, dependencies, tests, owner, recovery plan; freeze edits.
3. Publish to stage; review dependencies and warnings; configure stage connections and email routing.
4. Run T01 to T10, access tests and integration tests in stage; record approval.
5. Back up production, then publish; verify connections, schedules, permissions; run a limited smoke test.
6. Monitor logs and failed queues; keep a recovery plan. Publishing definitions and migrating data are separate.

Implementation and verification

Release gate	Acceptance evidence
Functional	Create, move status, notify tests pass
Security	Role tests pass; no public sensitive report
Integration	Correct CRM org; failures visible
Data	Backup verified; counts reconcile
Operations	Owner and recovery steps documented

Evidence and testing

E11: release notes, stage test log, approval record, backup reference, smoke test. If production is not authorized, mark publishing 'Not run'.

Process diagram

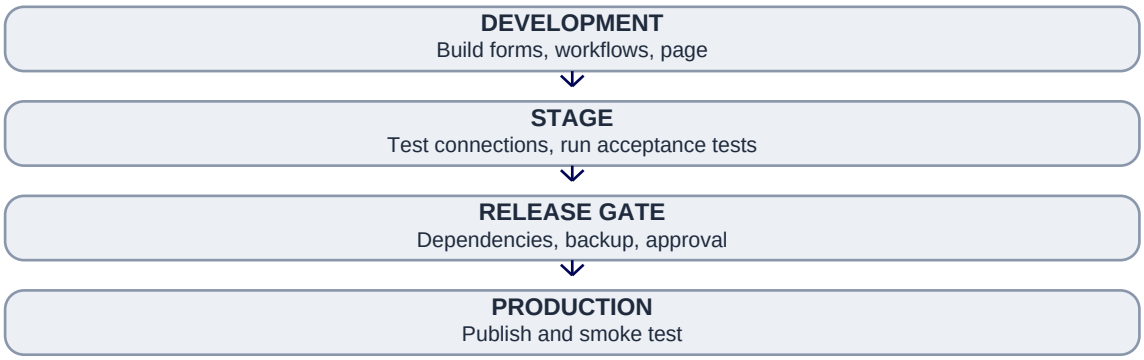

Generated explanatory diagram. It is not a screenshot of an executed workflow.

Result

Expected result and verification criteria. Release accepted only when gates pass; otherwise the blocked gate is recorded and no production deployment is claimed.
